


Project Info	
Project Name	EEM1 — DC3 Data Hall
Project Code / Site	EEM1-DC3 · VL0389
Project Location	Frankfurt am Main, Germany
Workspace Name	Workspace name
Workspace Location	Workspace location
Client	Client name
Project Duration	07/07/2025 - 18/07/2027 (742 days)

Report Details	
Report Type	DAB Report
Drawing	Externals-plan (sample)
Data Date Range	01/08/2026 - 31/10/2026
Content	4 zones · 1 locations · 27 tasks (26 scheduled) · 8 constraints · 2 markups
Team Members	Mitul L. (Planner), Nidhi Patel (Site Manager), Clark Kent (Structural Lead), Walter White (MEP Coordinator), Oliver (Logistics Lead), Bruce Wayne (HSE Advisor)

Export Info	
Exported By	Mitul L. — example@gmail.com
Export Date & Time	08/10/2026 - 20:50
Total Pages	18

Index		
S.No	Section	Page
MODEL VIEW		
1	Model view — zones, locations, markups & annotations	3
2	Annotation details	4
PROJECT DATA		
3	Weather	5
4	Zones	6
5	Locations	7
6	Tasks	8
7	Trades	10
8	High-risk activities (HRA)	11
9	Task status	12
10	Constraints	13
11	Markups	14
DASHBOARD		
12	Trade – task distribution	15
13	HRA – task distribution	16
14	Task status distribution	17
15	Zone & location matrix	18

How the data fits together: every task sits in one location (and optionally one zone) and carries a trade, one or more HRAs and a status.

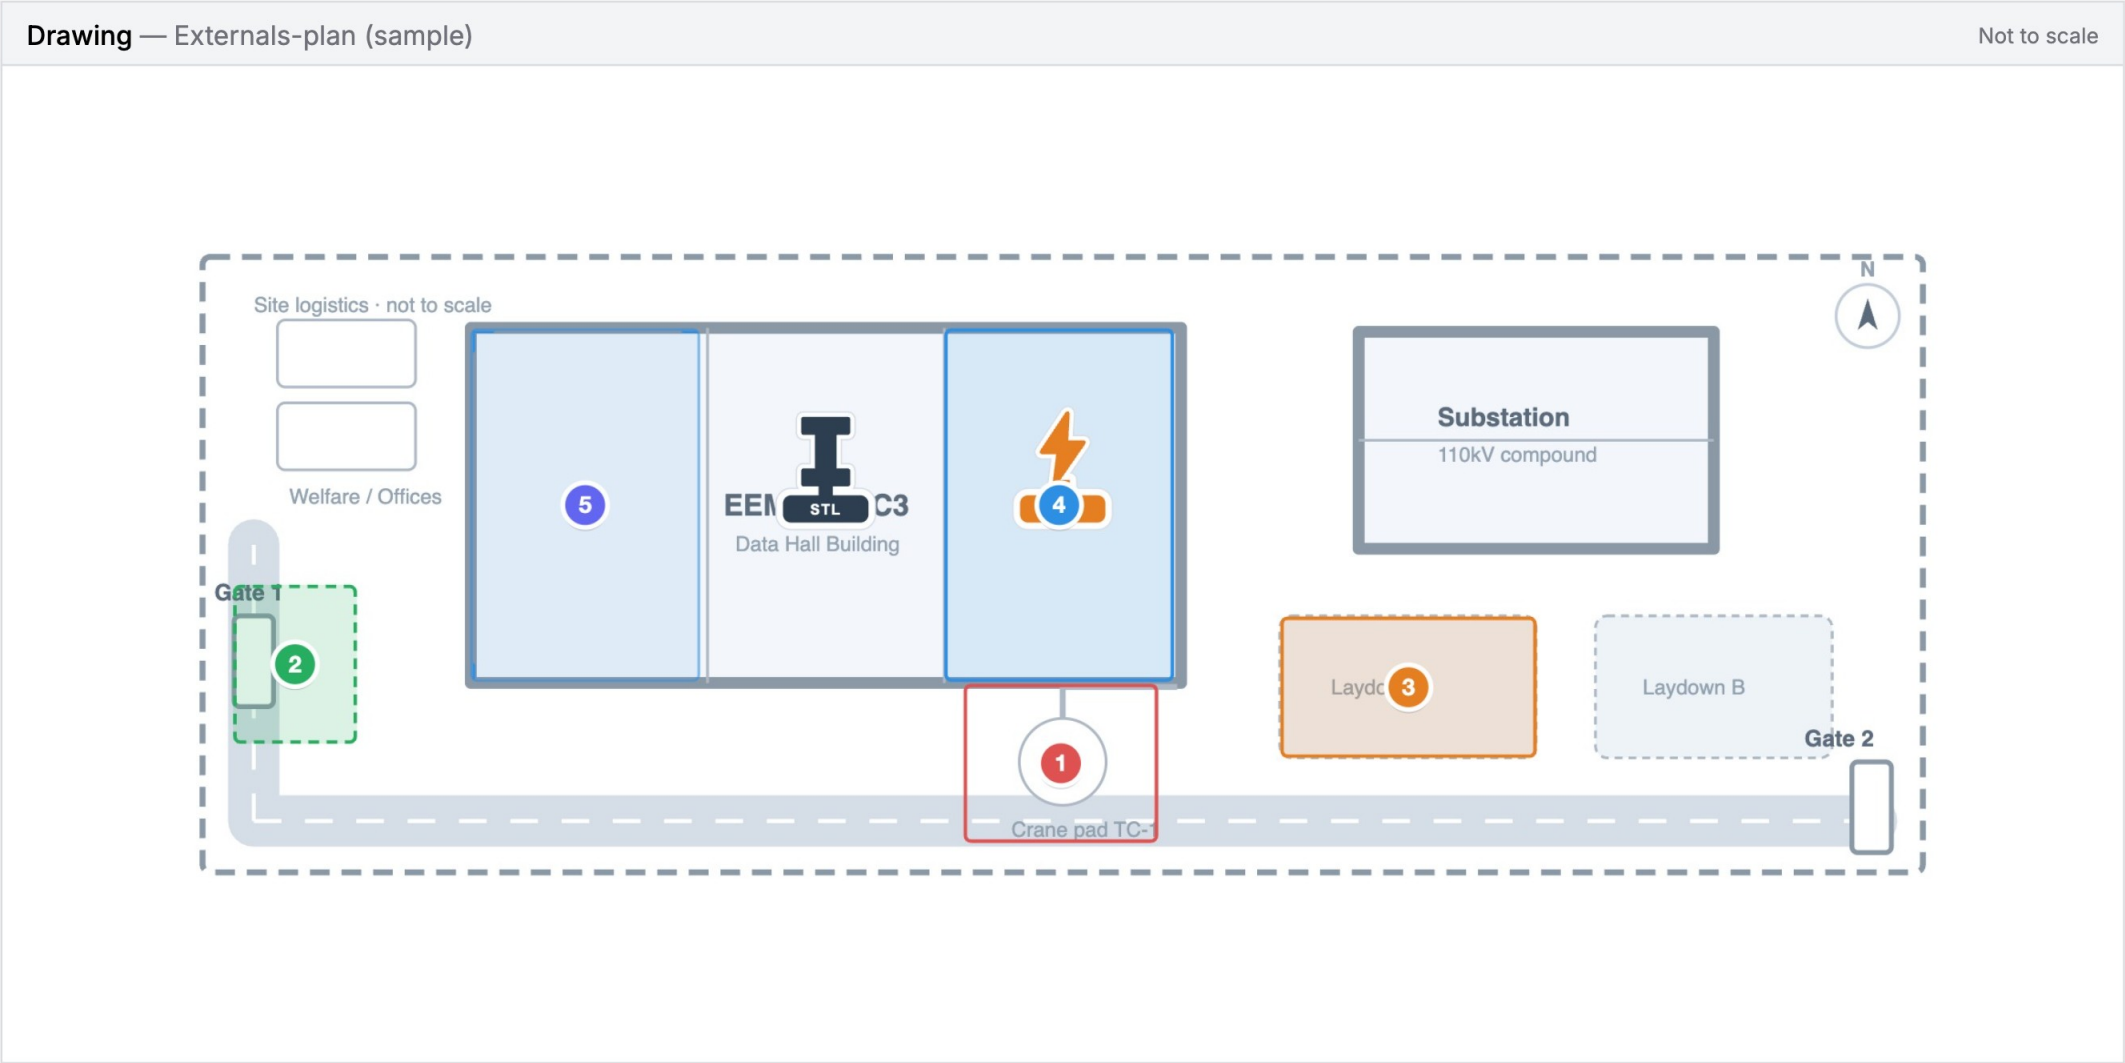

Zones & locations — number = annotation, details on page 4 · zone · location

1 Tower crane exclusion · zone

2 Gate 1 — deliveries · zone

3 Laydown yard C · zone

4 North Tower L02 — East Wing · zone

5 Level 2 — East · location

Markups — details on page 14

Trade sticker STL

Trade sticker ELE



Annotations										5 annotations	
No	Zone / Location	Type	Date range	HRA	Trades	Constraints	Tasks	Comments	Delayed		
1	Tower crane exclusion	Zone	27 Aug 26 - 20 Oct 26	⚠️🔥⚡🌧️	STR CIV MEP	5	9	0	🕒		
2	Gate 1 — deliveries	Zone	19 Aug 26 - 03 Sep 26	⚠️🌧️	CIV	0	3	0	—		
3	Laydown yard C	Zone	06 Sep 26 - 20 Oct 26	⚠️🌧️	STR CIV	0	4	0	—		
4	North Tower L02 — East Wing	Zone	12 Aug 26 - 23 Oct 26	⚠️🔊	CIV HVC FIT	1	6	0	🕒		
5	Level 2 — East	Location	19 Aug 26 - 20 Oct 26	⚠️🔥🔊⚡🌧️	STR CIV MEP	5	14	0	🕒		

No. matches the numbered markers on the model view (page 3). Delayed = at least one task is Stopped or has a Warning. Zone tasks also sit inside a location, so counts are not totalled across zones and locations.



Today — Thu 08 Oct 2026

Updated as of 10:30 AM

Frankfurt am Main, Germany

21°

12°

Sunny

Lifting OK — wind 6 m/s, limit 13 m/s

CURRENT CONDITIONS

Feels like

20°

Pressure

1018 hPa

DAY DETAILS

Sunrise

07:18

Wind

6 m/s

Humidity

58%

Sunset

19:14

Wind gust

11 m/s

Dew point

9°

UV index

4 (Moderate)

Visibility

10 km

Rain chance

5%

Precipitation

0 mm

7-day forecast							Wind limit for lifting 13 m/s
Day	Date	Condition	High / Low	Wind	Rain chance	Lifting	
Thu Today	08 Oct	Sunny	21° / 12°	6 m/s	5%	OK	
Fri	09 Oct	Sunny	19° / 11°	9 m/s	20%	OK	
Sat	10 Oct	Rain	17° / 10°	14 m/s	60%	Check lifting plan	
Sun	11 Oct	Rain	16° / 9°	16 m/s	70%	Check lifting plan	
Mon	12 Oct	Mostly sunny	18° / 10°	11 m/s	30%	OK	
Tue	13 Oct	Sunny	20° / 12°	7 m/s	10%	OK	
Wed	14 Oct	Sunny	22° / 13°	5 m/s	5%	OK	

Source: [Weather provider].

Exported by VisiLean

Mitul L. · 08/10/2026 - 20:50

Client name

EEM1 — DC3 Data Hall

5/18

Page

Zones										4 zones
No	Zone	Type	Linked to	Locations	Start	Finish	Tasks	Done	Constraints	Delayed
1	 Tower crane exclusion	 Exclusion	Takt	 Level 2 — East  Level 3 — Core	27 Aug 26	20 Oct 26	9	3	5	
2	 Gate 1 — deliveries	 Access	Gantt	 Level 2 — East  Basement 1 — Plant	19 Aug 26	03 Sep 26	3	3	0	—
3	 Laydown yard C	 Laydown	Takt	 Basement 1 — Plant	06 Sep 26	20 Oct 26	4	1	0	—
4	 North Tower L02 — East Wing	 Work Area	Gantt	 Level 2 — West	12 Aug 26	23 Oct 26	6	2	1	
Total							22	9	6	

No. matches the model view (page 3). 22 of the 27 tasks sit in a zone. Done = Completed or Approved.

Locations										1 location
No	Location	Hierarchy	Linked to	Zones	Start	Finish	Tasks	Done	Constraints	Delayed
5	 Level 2 — East	Building A > Level 2 > East Wing	Takt	Tower crane exclusion Gate 1 — deliveries	19 Aug 26	20 Oct 26	14	6	5	
	Total						14	6	5	

No. matches the model view (page 3). Every task belongs to exactly one location. Done = Completed or Approved.



Task register									1-14 of 27
Task ID	Task	Location	Zone	Trade	HRA	Start	Finish	Days	Status
 48415	Column rebar fixing — grid C/4-6	 Level 2 — East	 Tower crane exclusion	STR		07 Sep 26	14 Sep 26	8	 Approved
 48418	Slab formwork erection — bay 2	 Level 2 — East	 Tower crane exclusion	STR	 	27 Aug 26	07 Sep 26	12	 Completed
 48421	Slab concrete pour 4 (24 m³)	 Level 2 — East	 Tower crane exclusion	CIV	 	31 Aug 26	31 Aug 26	1	 Completed
 48424	Steel beam lift with TC-1	 Level 2 — East	 Tower crane exclusion	STR	 	23 Sep 26	28 Sep 26	6	 Started
 48427	Steel connection welding — L2	 Level 2 — East	 Tower crane exclusion	STR	 	21 Sep 26	29 Sep 26	9	 Warning
 48430	Temporary lighting install	 Level 2 — East	 Tower crane exclusion	MEP		03 Oct 26	06 Oct 26	4	 Ready
 48433	Cable tray first fix — east run	 Level 2 — East	—	MEP	 	16 Sep 26	29 Sep 26	14	 Started
 48436	Riser penetration sealing	 Level 2 — East	—	MEP	 	13 Oct 26	17 Oct 26	5	 Not Ready
 48439	Delivery bay kerb works	 Level 2 — East	 Gate 1 — deliveries	CIV	 	25 Aug 26	27 Aug 26	3	 Completed
 48442	Gate 1 hardstanding repair	 Level 2 — East	 Gate 1 — deliveries	CIV		19 Aug 26	20 Aug 26	2	 Approved
 48445	Edge protection check — L2 slab	 Level 2 — East	—	CIV		20 Sep 26	20 Sep 26	1	 Completed
 48448	Screed to plant plinths	 Level 2 — East	—	CIV		09 Oct 26	11 Oct 26	3	 Unassigned
 48451	Electrical containment — core wall	 Level 2 — East	—	MEP		—	—	—	 Unscheduled
 48454	Precast stair install	 Level 2 — East	 Tower crane exclusion	STR	 	19 Oct 26	20 Oct 26	2	 Force Ready

Task register									15–27 of 27
Task ID	Task	Location	Zone	Trade	HRA	Start	Finish	Days	Status
 48475	AHU ductwork mains	 Level 2 — West	 North Tower L02 — East Wing	HVC		16 Sep 26	07 Oct 26	22	 Started
 48478	Duct insulation	 Level 2 — West	 North Tower L02 — East Wing	HVC		20 Sep 26	29 Sep 26	10	 Stopped
 48481	Fan coil unit hanging	 Level 2 — West	 North Tower L02 — East Wing	HVC		16 Oct 26	23 Oct 26	8	 Ready
 48484	Raised floor pedestals	 Level 2 — West	 North Tower L02 — East Wing	FIT		27 Sep 26	30 Sep 26	4	 Not Ready
 48487	Floor screed — west wing	 Level 2 — West	 North Tower L02 — East Wing	CIV		27 Aug 26	29 Aug 26	3	 Completed
 48490	Blockwork — plant enclosure	 Level 2 — West	 North Tower L02 — East Wing	CIV		12 Aug 26	22 Aug 26	11	 Approved
 48499	Core wall formwork — lift 3	 Level 3 — Core	 Tower crane exclusion	STR		17 Sep 26	04 Oct 26	18	 Started
 48502	Core wall pour — lift 3	 Level 3 — Core	 Tower crane exclusion	STR		06 Oct 26	06 Oct 26	1	 Not Ready
 48532	Laydown ground bearing test	 Basement 1 — Plant	 Laydown yard C	CIV		06 Sep 26	07 Sep 26	2	 Completed
 48535	Laydown hardcore & compaction	 Basement 1 — Plant	 Laydown yard C	CIV		23 Sep 26	27 Sep 26	5	 Started
 48538	Rebar cage prefabrication	 Basement 1 — Plant	 Laydown yard C	STR		11 Sep 26	06 Oct 26	26	 Started
 48541	Generator plinth pour	 Basement 1 — Plant	 Laydown yard C	STR		20 Oct 26	20 Oct 26	1	 Ready
 48550	Delivery route marking — Gate 1	 Basement 1 — Plant	 Gate 1 — deliveries	CIV		03 Sep 26	03 Sep 26	1	 Approved

Trades								5 trades
S.No	Code	Trade	Trade lead	Tasks	Share	Done	Zones	Locations
1	CIV	Civil	Oliver	10	37%	8	Tower crane exclusion Gate 1 — deliveries Laydown yard C North Tower L02 — East Wing	Level 2 — East Basement 1 — Plant Level 2 — West
2	STR	Structural	Clark Kent	9	33%	2	Tower crane exclusion Laydown yard C	Level 2 — East Basement 1 — Plant Level 3 — Core
3	MEP	MEP services	Walter White	4	15%	0	Tower crane exclusion	Level 2 — East
4	HVC	HVAC	Walter White	3	11%	0	North Tower L02 — East Wing	Level 2 — West
5	FIT	Fit-out	Nidhi Patel	1	4%	0	North Tower L02 — East Wing	Level 2 — West
		Total		27	100%	10		

Each task has exactly one trade.



HRA							5 HRAs
S.No	Icon	High-risk activity	Tasks	Live now	Zones	Locations	
1		Working at Height	21	7	Tower crane exclusion Gate 1 — deliveries North Tower L02 — East Wing	Level 2 — East Level 2 — West	Basement 1 — Plant Level 3 — Core
2		Hot Works	2	1	Tower crane exclusion	Level 2 — East	
3		Confined Space Entry	3	2	North Tower L02 — East Wing	Level 2 — East	Level 2 — West
4		Electrical	3	1	Tower crane exclusion	Level 2 — East	
5		Adverse Weather	10	3	Tower crane exclusion Gate 1 — deliveries Laydown yard C	Level 2 — East Level 3 — Core	Basement 1 — Plant

A task can carry more than one HRA, so the Tasks column is not totalled. Live now = Started, Stopped or Warning today.



All status					27 tasks	
S.No	Mark	Status	Meaning		Tasks	Share
1		Unscheduled	No planned dates yet		1	4%
2		Unassigned	No task owner assigned		1	4%
3		Not Ready	Constraints or preceding work still open		3	11%
4		Ready	Constraints resolved — can start		3	11%
5		Force Ready	Released to start with open constraints		1	4%
6		Started	Work in progress on site		6	22%
7		Stopped	Work halted on site		1	4%
8		Warning	Alert raised — task at risk		1	3%
9		Rejected	Completion rejected at inspection		0	0%
10		Completed	Work finished — awaiting approval		6	22%
11		Approved	Completion approved		4	15%
		Total			27	100%

Each task has exactly one status. Shares are rounded to add up to 100%.



Constraints								8 active · 3 overdue
ID	Constraint	Category	Task	Location	Zone	Owner	Due	Status
#101	Riser layout drawings pending (RFI-021)	Information	 48436	 Level 2 — East	—	Walter White	22 Sep 26	Overdue
#102	Steel members delivery delayed	Material	 48424	 Level 2 — East	 Tower crane exclusion	Oliver	29 Sep 26	Open
#103	Crane lift plan awaiting approval	Permit	 48454	 Level 2 — East	 Tower crane exclusion	Bruce Wayne	30 Sep 26	Open
#104	Hot works permit for steel connections	Permit	 48427	 Level 2 — East	 Tower crane exclusion	Clark Kent	23 Sep 26	Overdue
#105	Scaffold access blocked by crane zone	Space / access	 48499	 Level 3 — Core	 Tower crane exclusion	Nidhi Patel	02 Oct 26	Open
#106	Cable tray clashes with supply duct	Design	 48433	 Level 2 — East	—	Walter White	30 Sep 26	Open
#107	Duct insulation material short-shipped	Material	 48478	 Level 2 — West	 North Tower L02 — East Wing	Walter White	24 Sep 26	Overdue
#110	Core wall pour sequence to confirm	Preceding work	 48502	 Level 3 — Core	 Tower crane exclusion	Clark Kent	03 Oct 26	Open

A constraint is raised on a task and inherits its location and zone.




Markups					2 markups
Markup	Detail	Placed in	Added by	Date	
 Trade sticker	STL · Steel	—	—	—	
 Trade sticker	ELE · Electrical	 North Tower L02 — East Wing	—	—	

Markup icons match the model view (page 3).




Tasks per trade

27 tasks

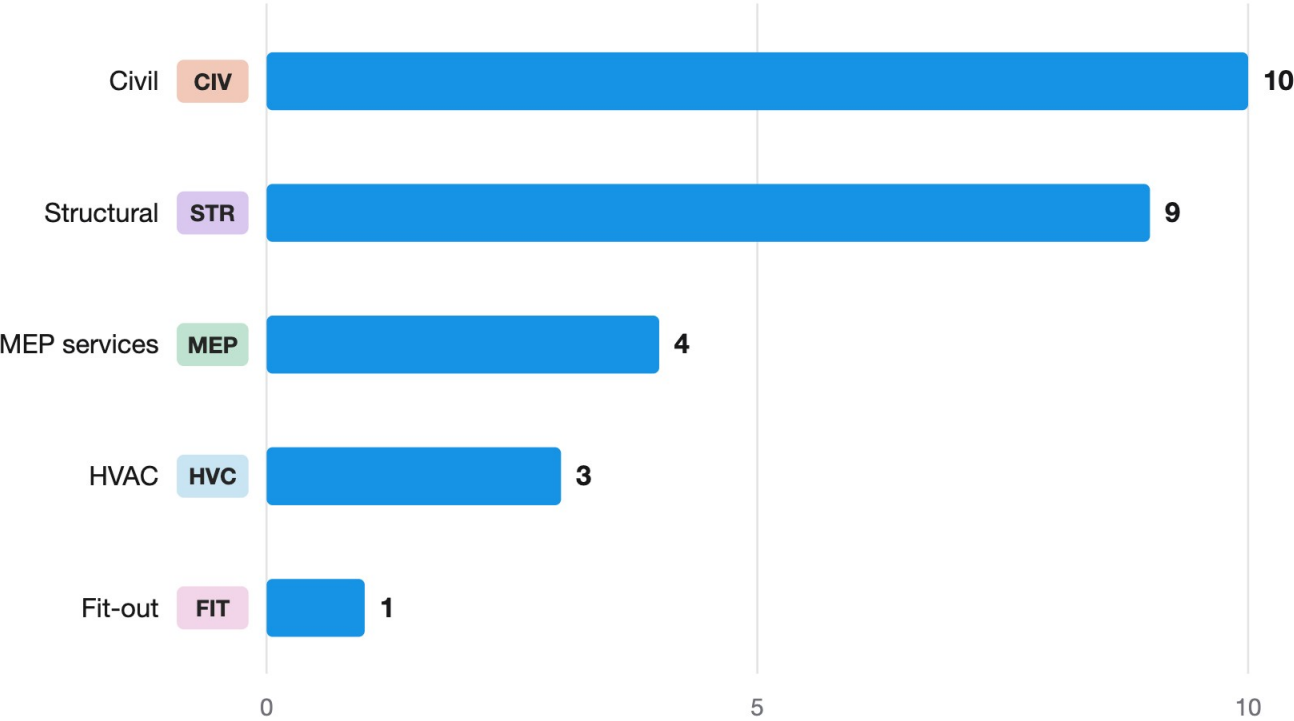


Tasks per high-risk activity

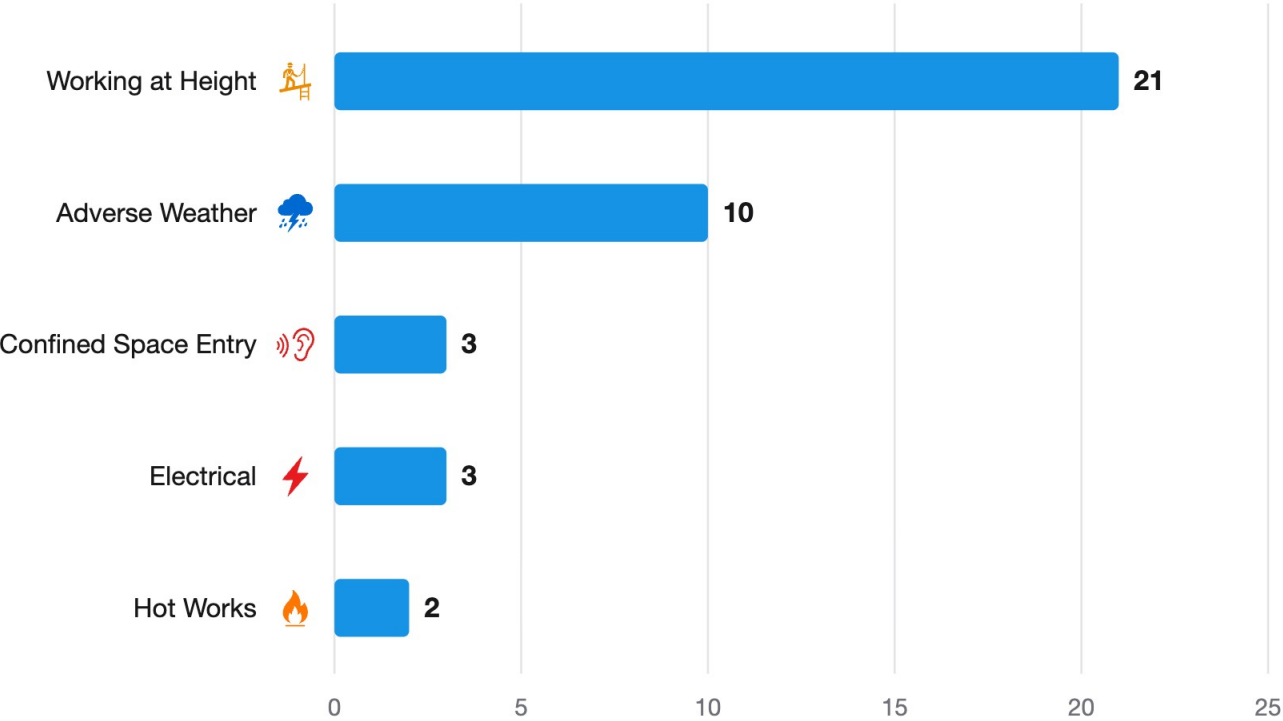


A task can carry more than one HRA.



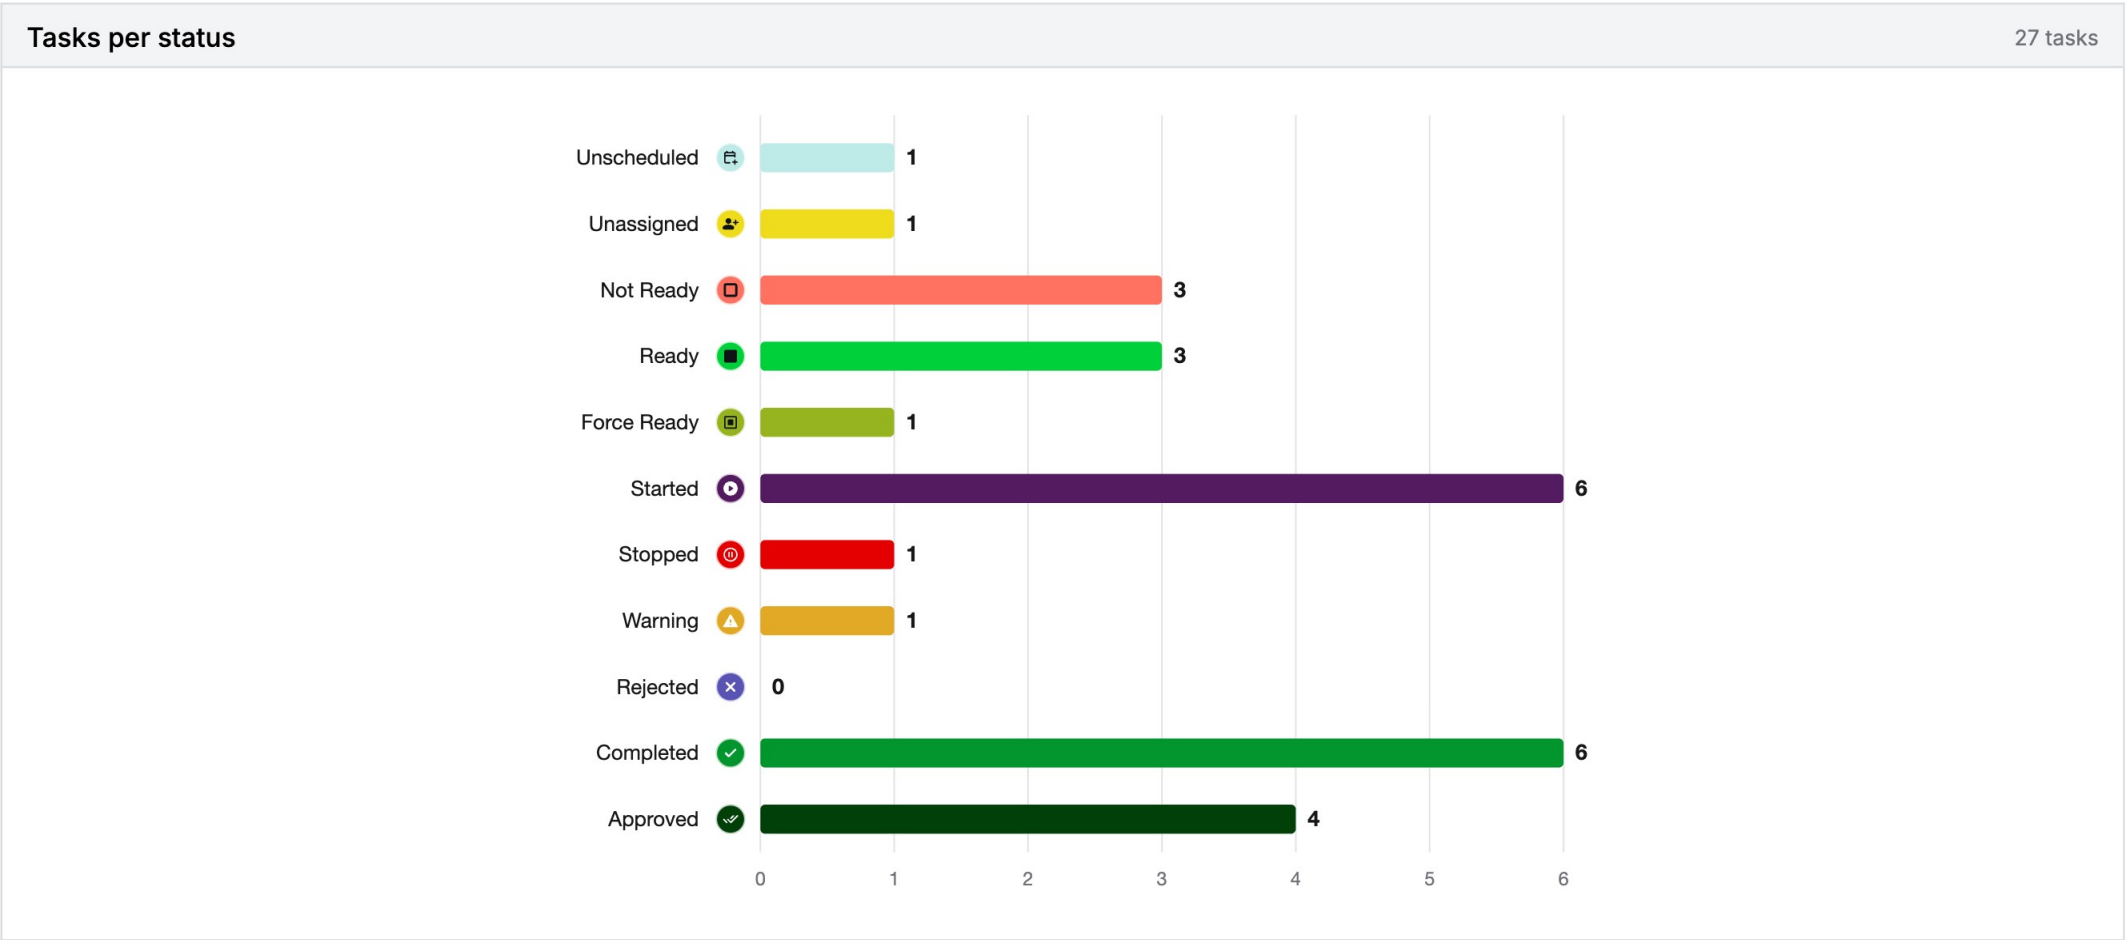

Bar colours follow the VisiLean status colours.



HRA by zone and location						
Zone / Location	 Working at Height	 Hot Works	 Confined Space Entry	 Electrical	 Adverse Weather	All tasks
ZONES						
1 Tower crane exclusion	8	1	—	1	5	9
2 Gate 1 — deliveries	1	—	—	—	3	3
3 Laydown yard C	4	—	—	—	2	4
4 North Tower L02 — East Wing	5	—	2	—	—	6
LOCATIONS						
5 Level 2 — East	10	2	1	3	6	14
All tasks with this HRA	21	2	3	3	10	27
0  10+ tasks						

Cells show how many tasks in each zone / location carry that HRA. A task can carry more than one HRA, and zone tasks also sit inside a location. No. matches the model view (page 3).
